



VERTICAL GAP BETWEEN TURBINE GUIDE BEARING SEGMENTS

QCR 2207

PROJECT : Seven Mile

Unit: 4

ITP step no.: 1719


Measurement Instruments

Ambient Temperature

Feeler gauge

Before: _____


After: _____

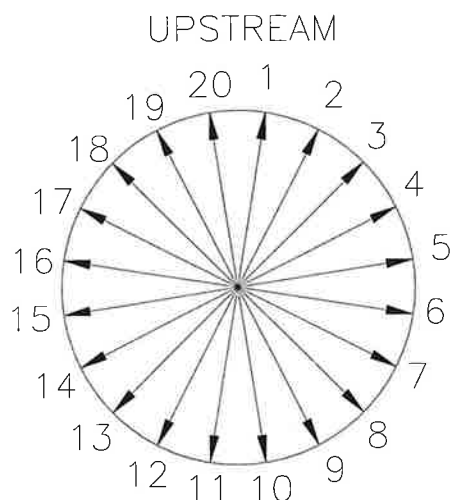

SEGMENTS	GAP (mm)	SEGMENTS	GAP (mm)
1-2	2.9	14-15	2.6
2-3	2.25	15-16	2.15
3-4	2.45	16-17	3.25
4-5	2.5	17-18	2.75
5-6	3.15	18-19	2.65
6-7	2.45	19-20	2.9
7-8	2.45	20-1	2.25
8-9	2.4		
9-10	2.4		
10-11	2.6		
11-12	2.2		
12-13	2.15		
13-14	2.1		

TOLERANCE

2.5 +/- 0.8 mm

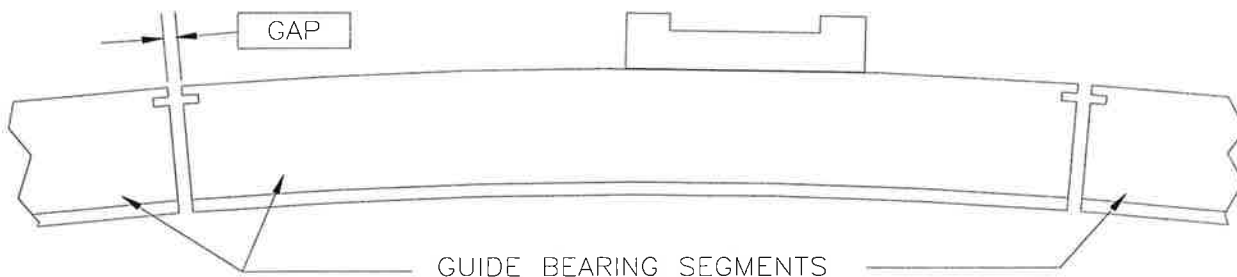

RECEIVED
JAN 30 2003
JA

Measured by.: John Willman (Jan 27th 2003)

GE Repres.: Philippa McIntyre (Jan 24th 2003)

Cust. Repres.: _____ (/ /)

GE Canada
International Inc.

Reference NC no.: _____

Comments: _____

Rev.: 0

Date: 03-01-06



TURBINE GUIDE BEARING CLEARANCES

QCR 2202

PROJECT: Seven Mile

Unit: 4

ITP step no.: 1721

Runner blocked at 0°

Runner free at 0°

Runner free at 180°

☐
☒
☐

During adjustments.



Measurement Instruments

Feeler gauge

Ambient Temperature

Before: _____

After: _____

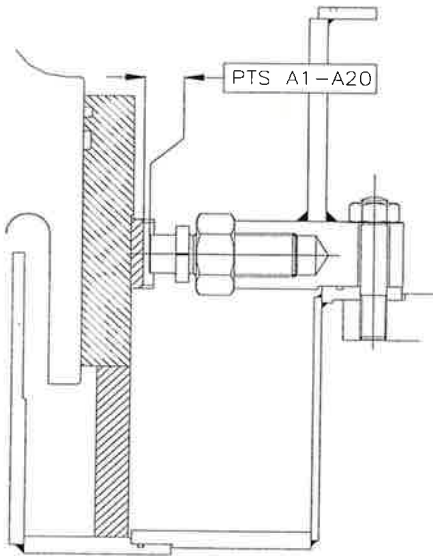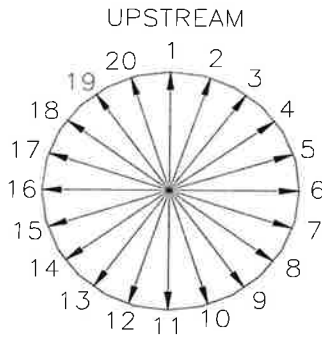

PTS	A (mm)
1	0.25
2	0.25
3	0.25
4	0.25
5	0.25
6	0.23
7	0.25
8	0.25
9	0.25
10	0.25
11	0.25
12	0.25
13	0.25
14	0.25
15	0.25
16	0.25
17	0.23
18	0.25
19	0.25
20	0.25

	Calculated (mm)	Tolerance (mm)
Concentricity *	0.001	0.05

* For runner at 0° and 180°

Nominal clearance*
0.20 to 0.25mm

* Runner blocked at 0°



Measured by.: *John Willmann* (Jan 27 2003)

GE Repres.: *John Willmann* (Jan 28 2003)

Cust. Repres.: _____ (/ /)

GE Canada
International Inc.

Reference NC no.: _____
Comments: _____

Rev.: 0
Date: 02/11/26



TURBINE GUIDE BEARING CLEARANCES

QCR 2202

PROJECT: Seven Mile


Unit: 4

ITP step no.: 1721

Runner blocked at 0°

Runner free at 0°

Runner free at 180°



Final



Measurement Instruments

Feeler gauge

Ambient Temperature

Before: _____

After: _____

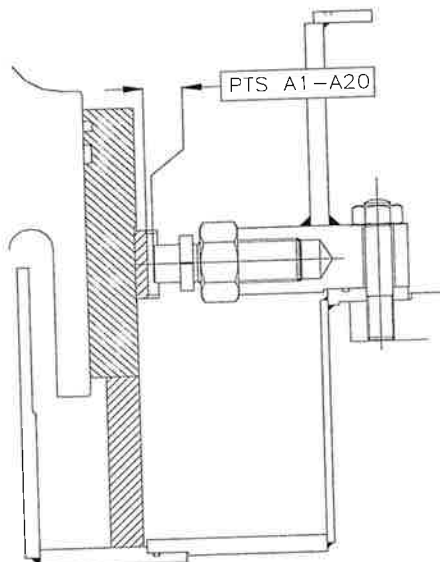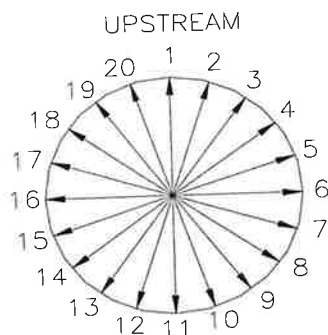

PTS	A (mm)
1	0,27
2	0,24
3	0,27
4	0,24
5	0,27
6	0,29
7	0,22
8	0,25
9	0,29
10	0,27
11	0,27
12	0,24
13	0,27
14	0,27
15	0,24
16	0,23
17	0,29
18	0,24
19	0,24
20	0,22

	Calculated (mm)	Tolerance (mm)
Concentricity *	0,01	0.05

* For runner at 0° and 180°

Nominal clearance*
0.20 to 0.25mm

* Runner blocked at 0°



Measured by.: John Willman (Feb/1st/2003)

GE Repres.: Jeff Lemon (Feb/3rd/2003)

Cust. Repres.: (/ /)

GE Canada
International Inc.

Reference NC no.: _____

Comments: _____

Rev.: 0

Date: 02/11/26



TURBINE GUIDE BEARING CLEARANCES

QCR 2202

PROJECT: Seven Mile

Unit: 4

ITP step no.: 1721

Runner blocked at 0°

Runner free at 0°

Runner free at 180°

☐
☒
☒

Final



Measurement Instruments

Feeler gauge

Ambient Temperature

Before: _____

After: _____

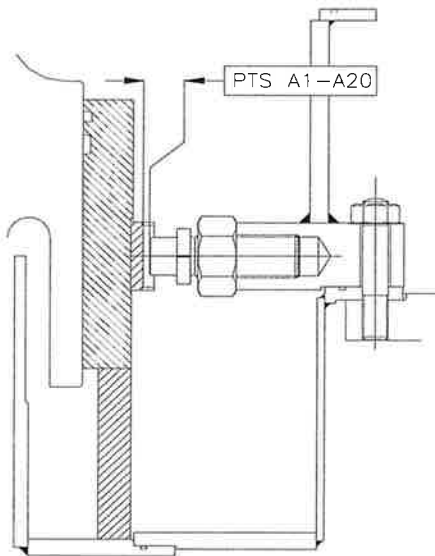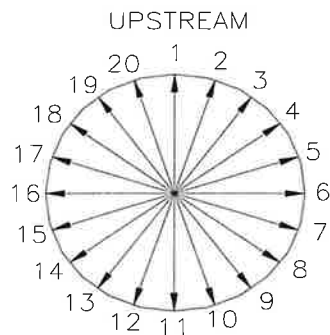

PTS	A (mm)
1	0.23
2	0.20
3	0.25
4	0.24
5	0.27
6	0.24
7	0.24
8	0.23
9	0.22
10	0.27
11	0.26
12	0.24
13	0.24
14	0.23
15	0.24
16	0.27
17	0.22
18	0.24
19	0.24
20	0.23

	Calculated (mm)	Tolerance (mm)
Concentricity *	0.01	0.05

* For runner at 0° and 180°

Nominal clearance*
0.20 to 0.25mm

* Runner blocked at 0°



Measured by.: John Willman (Feb 1st 2003)
GE Repres.: Jeff Leman (Feb 3rd 2003)
Cust. Repres.: [Signature] (/ /)

GE Canada
International Inc.

Reference NC no.: _____
Comments: _____

Rev.: 0
Date: 02/11/26



GENERAL INSPECTION REPORT

QCR 004

PROJECT: Seven Mile

Unit: 4

ITP step no.: 1722

EQUIPMENT : Torquing of bearing seals

The set screws on the bearing seals have been torqued at a value of 15 N.m lubricated.

RECEIVED
FEB 12 2003
C/A

Measured by.: F. Boulet (/ /)
GE Repres.: [Signature] (Feb 12th 2003)
Cust. Repres.: [Signature] (/ /)

GE Canada
International Inc.

Reference NC no.: _____

Comments: _____

Rev.: 0

Date: 07/23/01



GENERAL INSPECTION REPORT

QCR 004

PROJECT: Seven Mile

Unit: 4

ITP step no.: 1724

EQUIPMENT : Torquing of bearing cover plates

The bolts holding the turbine guide bearing cover plates have been torqued at a value of 40 N.m lubricated.

RECEIVED
FEB 12 2003
CA

Measured by.: F. Boulet (/ /)
GE Repres.: [Signature] Feb 12th 2003
Cust. Repres.: [Signature] (/ /)

GE Canada
International Inc.

Reference NC no.: _____

Comments: _____

Rev.: 0

Date: 07/23/01



GENERAL INSPECTION REPORT

QCR 004

PROJECT: Seven Mile

Unit: 4

ITP step no.: 1725

EQUIPMENT : Gap between the shaft and the TGB covers.

PTS	GAP (mm)
1	3,48
2	3,49
3	3,27
4	3,27
5	3,27
6	3,47
7	3,48
8	3,48

	TOLERANCE (mm)	CALCULATED (mm)
CONCENTRICITY	0,5	0,13

Turbine Shaft

PTS 1-8

Cover



Measured by.: Jake Zondervan Jan / /)
GE Repres.: Douglas Everett
Cust. Repres.: Michael J. Johnson Feb 4th / 2003 (/ /)

GE Canada
International Inc.

Reference NC no.: _____

Comments: _____

Rev.: 0

Date: 07/23/01



GENERAL INSPECTION REPORT

QCR 004

PROJECT: Seven Mile

Unit: 4

ITP step no.: 1728

EQUIPMENT : Gap between packing segments and shaft

A feeler gauge of 0,50 mm enters between the packing segments and the shaft.

RECEIVED
FEB 12 2003

Ch

Measured by.:	<u>P. Lamontagne</u> (/ /)
GE Repres.:	<u>[Signature]</u> (/ /)
Cust. Repres.:	<u>[Signature]</u> (/ /)

GE Canada
International Inc.

Reference NC no.: _____

Comments: _____

Rev.: 0

Date: 07/23/01



FINAL INSPECTION

QCR 003

PROJECT: Seven Mile

Unit: 4

ITP step no.: ~~1730~~

1730

THIS FORM MUST BE COMPLETED BY THE TECHNICAL DIRECTOR, QUALITY ASSURANCE OR HIS REPRESENTATIVE.

THIS FORM MUST BE COMPLETED AT THE END OF WORK FOR EACH SECTION IN THE INSPECTION AND THE TEST PLAN.

ALL NON CONFORMANCES, DISCREPANCIES, ETC. MUST BE CORRECTED BEFORE COMPLETING THIS FORM.

ONLY THE SPECIFIED ITEMS IN CONTRACT ARE SUBMITTED TO THE FINAL INSPECTION.

	YES	NO	N/A
ALL WORK WAS COMPLETED IN CONFORMITY WITH INSTALLATION MANUAL AND DRAWINGS.	✓		
THE FINAL PRODUCT HAVE BEEN INSPECTED AT THE END OF WORK AND IS IN CONFORMITY WITH CONTRACT REQUIREMENTS.	✓		
ALL NON CONFORMANCES HAVE BEEN CORRECTED ACCORDING TO THE DISPOSITION INSTRUCTIONS.	✓		
ALL CORRECTIVE ACTION REQUESTS HAVE BEEN CORRECTED AT THE CUSTOMER SATISFACTION.	✓		
ALL QUALITY ASSURANCE REPORTS HAVE BEEN COMPLETED ACCORDING TO I.T.P.	✓		
ALL FORMS HAVE BEEN REVISED AND APPROVED BY THE QUALITY ASSURANCE REPRESENTATIVE.	✓		
APPROVAL OF ENGINEERING HAVE BEEN OBTAINED WHEN NECESSARY.	✓		
APPROVAL OF CUSTOMER OR HIS REPRESENTATIVE HAVE BEEN OBTAINED WHEN NECESSARY.	✓		

REF. N.C. AND C.A.R. NB.: NC-5MI-U04-023COMMENTS :

RECEIVED

MAR 03 2003
CHMeasured by.: Frank Smith (02/26/03)GE Repres.: Frank Smith (02/26/03)Cust. Repres.: Chait by Mr. LockGE Canada
International Inc.Reference NC no.: _____
Comments: _____Rev.: 0
Date: 07/23/01
